Executive Summary

Status as of Month 7 | AI-Synthesized Data

Schedule & Risk >

SPI

0.93

CPI

0.95

Overdue

7

Status Month
7

At Month 7, Project HORIZON is 7% behind schedule and spending $1.06 for every $1.00 of work completed, forecasting a $271K overrun (5.4% of budget).

Performance Quadrant

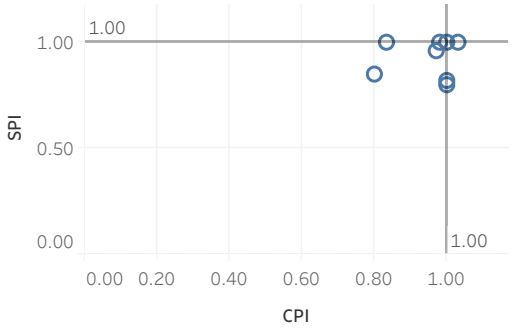

KPI Table

WP ID	WP Name	PV to Date	EV to Date	AC to Date	SPI	CPI	EAC	VAC
WP01	F-15 Support Ai..	$566,100	$566,100	$577,422	1.00	0.98	$918,000	-$18,000
WP02	F-18 Support Ai..	$629,000	$603,840	$621,955	0.96	0.97	$1,030,000	-$30,000
WP03	Ground Test Fa..	$618,100	$494,480	$494,480	0.80	1.00	$700,000	$0
WP04	Flight Simulator	$450,000	$382,500	$478,125	0.85	0.80	$750,000	-$150,000
WP05	Radar Tracking	$550,000	$550,000	$533,500	1.00	1.03	$533,500	$16,500
WP06	Optical Tracking	$384,300	$384,300	$461,160	1.00	0.83	$540,000	-$90,000
WP07	Airborne Meas..	$250,000	$205,000	$205,000	0.82	1.00	$500,000	$0
WP08	Data Analysis ..	$123,900	$123,900	$123,900	1.00	1.00	$300,000	$0
Grand Total		$3,571,400	$3,310,120	$3,495,542	0.93	0.95	$5,271,500	-$271,500

Cumulative Curve



WHAT TO DO

(1) **WP04 Flight Simulator** (SPI 0.85, CPI 0.80, -$150K): resolve the vendor integration risk (R01, R02) first. It is behind and over budget.

(2) **WP07 AIrborne Measurements** (SPI 0.82): expedite the sensor delivery (R05, the top-scored risk). The risk plausibly explains the schedule slip.

(3) **WP06 Optical Tracking** (CPI 0.83): renegotiate camera repair cost (R07). On schedule, over budget...

Schedule & Risk

Status as of Month 7 | AI-Synthesized Data

< Executive Summary

Task Timeline

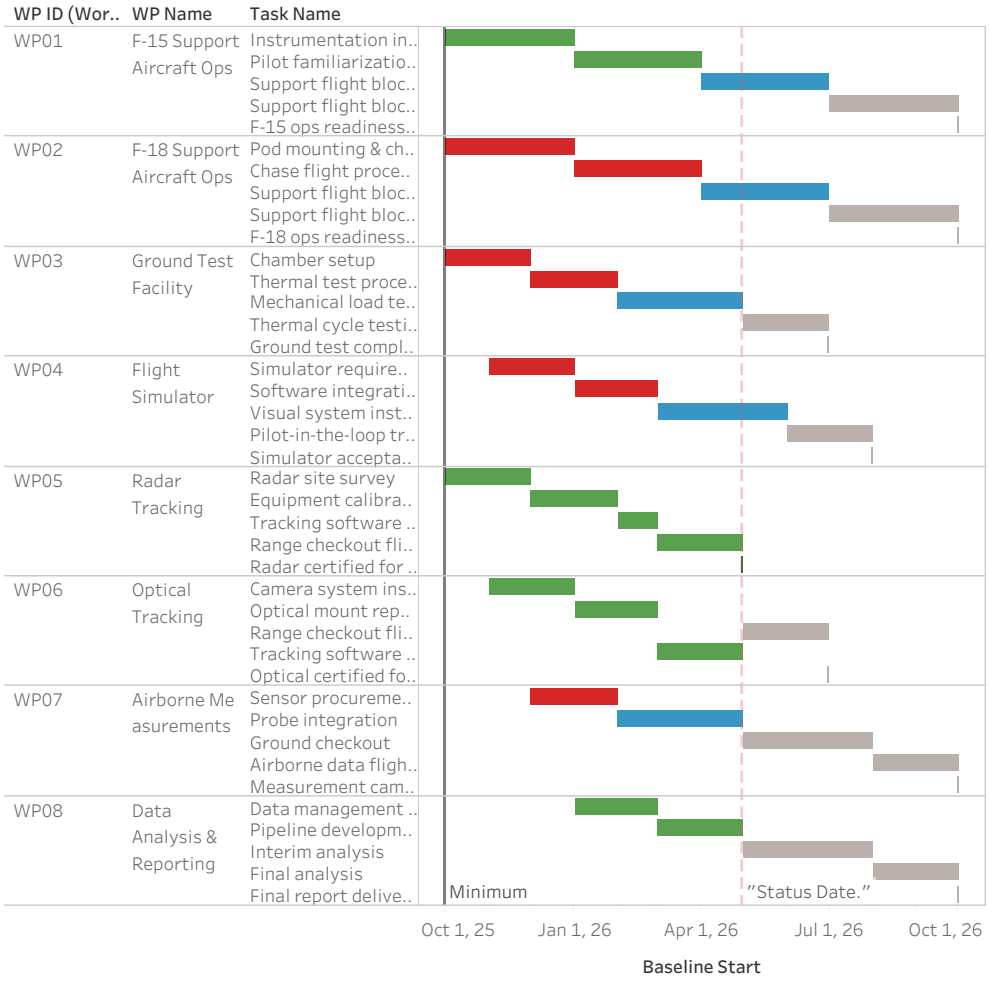

Risk Heatmap

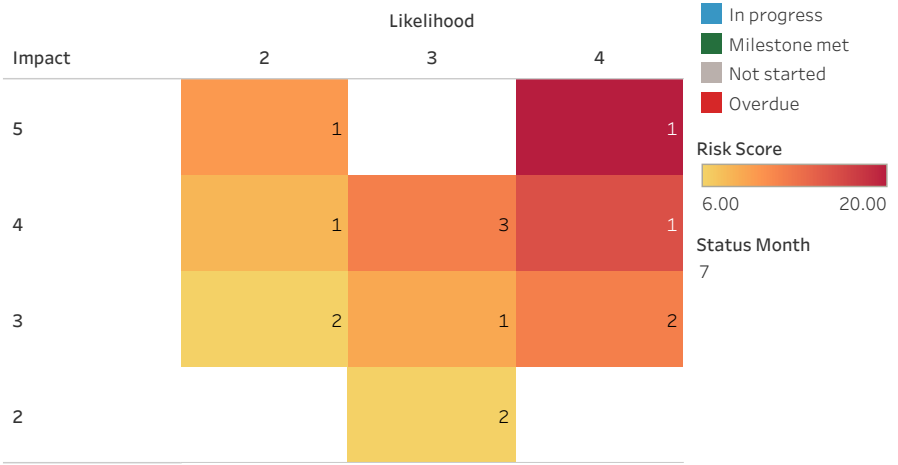

Top Risks

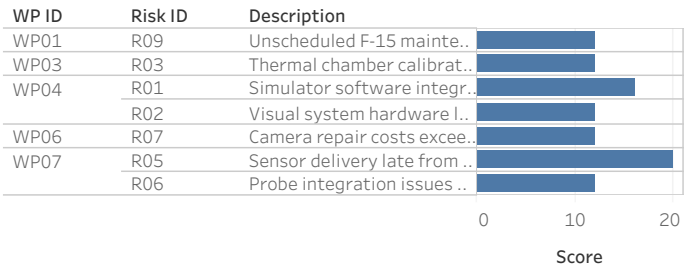

Insights

*Seven overdue tasks cluster in four work packages, and the top-scored risk (late sensors, score 20) sits in Airborne Measurements, which is running 18% behind schedule.
